

Work Order ID 138686

138686

Page 1

Monday, November 09, 2015 8:39:09 AM

Item ID: D3822-2KGY Accept ***N900040100*** Setup Start ***NS1***
Revision ID: Stop ***NS2***
Item Name: Vertical Tunnel, RH
Start Date: 11/9/2015 Start Qty: 2.00 ***2*** Cust Item ID:
Required Date: 11/9/2015 Req'd Qty: 2.00 ***2*** Customer:
Reference:

Approvals: Process Plan: ML3 Date: NOV 09 2015 Tooling: _____ Date: _____
QC: _____ Date: _____ SPC (Y/N): _____ Date: _____
Run Start ***NR1***
Stop ***NR2***

Sequence ID/ Work Center ID	Operation Description	Set Up/ Run Hours	Tool ID	Tool #	Plan Code	Accept Qty	Reject Qty	Reject Number	Insp. Stamp
--------------------------------	--------------------------	----------------------	---------	--------	--------------	---------------	---------------	------------------	----------------

Draw Nbr	Revision Nbr
D3822-2	Rev. C

100		0.00							DAS 07 9-89
100									
HandThermo	Memo	0.01							
Hand Finishing Thermoforming	1-Cut Sheet to required Blank size								15/11/06

105		0.00							DAS 07 9-89
105									
HandThermo	Dry Material	0.00							
Hand Finishing Thermoforming	Memo								15/11/06
	Dry Sheet as per QSI022 KYDEX								

Temp: 152 deg. F
Time IN: 5:00 PM
Time OUT: 6:00 AM

OCT 05 2015
Per.....

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____		DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐		AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐					
Date :		Step #:		QTY Effective :			MRB (QSI042) Approval Completed By Lead hand / Supervisor Approval Verification QC / QA Coordinator Approval		
Description Work Order Deviation				Disposition					

Root Cause				FAULT CATEGORY			
Environment	☐	No Re-verification	☐	Pressure/Forced	☐	Temperature/Cure	☐
Design	☐	Operator	☐	Bending	☐	Set-up	☐
Doc/Data	☐	Offset/Setup	☐	Centre Not Concentric	☐	BOM/Route	☐
Equip/Tooling	☐	Supplier	☐	Cracks	☐	Broken/Damage/Defect	☐
Handling/Pre	☐	Training	☐	Crimp/Kink/Ripple/Wave	☐	Inspection Incomplete/Unqualified	☐
Material	☐	Use for Testing	☐	Cuffs	☐	Contamination	☐
Internal Transport	☐	Poor Information	☐	Crushing	☐	Countersink	☐
Tribal Knowledge	☐	Rushing	☐	Heat Treat	☐	Cut Too Short	☐
LOA	☐	Product Improvement	☐	Wave/Twist in Tube	☐	Instructions Incomplete/Unclear	☐
Substation	☐	Process Improvement	☐	Marks/Chatter	☐	Drill Holes	☐
Past Expiry Date	☐	Manufacturing Process	☐	OTHER : _____			
Misidentified	☐	Past Due	☐				

Monday, November 09, 2015 8:39:09 AM

138686

Page 2

N900040100

Setup Start *NS1*

Stop *NS2*

Start Date: 11/9/2015 **Start Qty:** 2.00 ***2***

Cust Item ID:

Required Date: 11/9/2015 **Req'd Qty:** 2.00 ***~***

Customer:

Reference:

Run Start *NR1*

Approvals: **Process Plan:** _____ **Date:** _____ **Tooling:** _____ **Date:** _____

Stop *NR2*

QC: _____ Date: _____ SPC (Y/N): _____ Date: _____

Sequence ID/ Work Center ID	Operation Description	Set Up/ Run Hours	Tool ID	Tool #	Plan Code	Accept Qty	Reject Qty	Reject Number	Insp. Stamp
110		0.00							07 9-89

1 1 0

Thermoform

Thermoforming Machine

Memo

1-Machine Set-Up
2-Pre-heat Tool to required temp.
3-Thermoform as per Dwg and Folio #FTA026 using tool DT9074

Dwg Rev: C

Folio Rev: 13

Visually inspect for proper formation of each part

140

140

HandThermo

Hand Finishing Thermoforming

Memo

1-Trim to finished dimensions as per Dwg

DAS
07
9-89

x2 15/4/01

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____		DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐		AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐					
Date :		Step #:		QTY Effective :			MRB (QSI042) Approval Completed By Lead hand / Supervisor Approval Verification QC / QA Coordinator Approval		
Description Work Order Deviation				Disposition					

Root Cause				FAULT CATEGORY							
Environment	☐	No Re-verification	☐	Pressure/Forced	☐	Temperature/Cure	☐	Power Loss/Surge	☐	Positioned Wrong	☐
Design	☐	Operator	☐	Bending	☐	Set-up	☐	Folio/Program	☐	Outside Dimensions	☐
Doc/Data	☐	Offset/Setup	☐	Centre Not Concentric	☐	BOM/Route	☐	Grain	☐	Over/Under tolerance	☐
Equip/Tooling	☐	Supplier	☐	Cracks	☐	Broken/Damage/Defect	☐	Weld	☐	Part Incorrect	☐
Handling/Pre	☐	Training	☐	Crimp/Kink/Ripple/Wave	☐	Inspection Incomplete/Unqualified	☐	Wrong Stock Pulled	☐	Part Lost/Missing	☐
Material	☐	Use for Testing	☐	Cuffs	☐	Contamination	☐	Out of Sequence	☐	Part Moved	☐
Internal Transport	☐	Poor Information	☐	Crushing	☐	Countersink	☐	Off-set	☐	Drawing	☐
Tribal Knowledge	☐	Rushing	☐	Heat Treat	☐	Cut Too Short	☐	Mislabeled	☐	Finish	☐
LOA	☐	Product Improvement	☐	Wave/Twist in Tube	☐	Instructions Incomplete/Unclear	☐	Fit/Function	☐	Misread	☐
Substation	☐	Process Improvement	☐	Marks/Chatter	☐	Drill Holes	☐	Misaligned/off center	☐	Turning Sequence	☐
Past Expiry Date	☐	Manufacturing Process	☐	OTHER : _____							
Misidentified	☐	Past Due	☐								

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____		DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐ Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging Supplier ☐ Engineering Quality ☐ Other ☐		AGAINST DEPARTMENT/PROCESS					
Date :		Step #:		QTY Effective :			MRB (QSI042) Approval		
Description Work Order Deviation				Disposition				Completed By	
								Lead hand / Supervisor Approval Verification	
								QC / QA Coordinator Approval	
Root Cause		FAULT CATEGORY							
Environment ☐ Design ☐ Doc/Data ☐ Equip/Tooling ☐ Handling/Pre ☐ Material ☐ Internal Transport ☐ Tribal Knowledge ☐ LOA ☐ Substation ☐ Past Expiry Date ☐ Misidentified ☐	No Re-verification ☐ Operator ☐ Offset/Setup ☐ Supplier ☐ Training ☐ Use for Testing ☐ Poor Information ☐ Rushing ☐ Product Improvement ☐ Process Improvement ☐ Manufacturing Process ☐ Past Due ☐	Pressure/Forced ☐ Bending ☐ Centre Not Concentric ☐ Cracks ☐ Crimp/Kink/Ripple/Wave ☐ Cuffs ☐ Crushing ☐ Heat Treat ☐ Wave/Twist in Tube ☐ Marks/Chatter ☐	Temperature/Cure ☐ Set-up ☐ BOM/Route ☐ Broken/Damage/Defect ☐ Inspection Incomplete/Unqualified ☐ Contamination ☐ Countersink ☐ Cut Too Short ☐ Instructions Incomplete/Unclear ☐ Drill Holes ☐	Power Loss/Surge ☐ Folio/Program ☐ Grain ☐ Weld ☐ Wrong Stock Pulled ☐ Out of Sequence ☐ Off-set ☐ Mislabeled ☐ Fit/Function ☐ Misaligned/off center ☐	Positioned Wrong ☐ Outside Dimensions ☐ Over/Under tolerance ☐ Part Incorrect ☐ Part Lost/Missing ☐ Part Moved ☐ Drawing ☐ Finish ☐ Misread ☐ Turning Sequence ☐	OTHER : ☐			

Work Order ID 138686***138686***

Page 4

Monday, November 09, 2015 8:39:09 AM

Item ID: D3822-2KGY

Accept

N900040100Setup Start ***NS1***

Revision ID:

Stop ***NS2***

Item Name: Vertical Tunnel, RH

Start Date: 11/9/2015 Start Qty: 2.00

2

Cust Item ID:

Required Date: 11/9/2015 Req'd Qty: 2.00

2

Customer:

Reference:

Approvals: Process Plan: _____ Date: _____ Tooling: _____ Date: _____

Run Start ***NR1***

QC: _____ Date: _____ SPC (Y/N): _____ Date: _____

Stop ***NR2***

Sequence ID/ Work Center ID	Operation Description	Set Up/ Run Hours	Tool ID	Tool #	Plan Code	Accept Qty	Reject Qty	Reject Number	Insp. Stamp
--------------------------------	--------------------------	----------------------	---------	--------	--------------	---------------	---------------	------------------	----------------

180

QC21- Final Inspection - Work Order Release

0.00

180

QC

Memo

0.00

Quality Control

MLJ NOV 10 2015

MLJ NOV 09 2015

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____		DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐		AGAINST DEPARTMENT/PROCESS <table style="width: 100%; border: none;"> <tr> <td style="width: 15%;">Skid-tube ☐</td> <td style="width: 15%;">Cross tube ☐</td> <td style="width: 15%;">Water Jet ☐</td> <td style="width: 15%;">Engineering ☐</td> </tr> <tr> <td>Machining ☐</td> <td>Small Fab ☐</td> <td>Prod. Eng. Coord. ☐</td> <td>Quality ☐</td> </tr> <tr> <td>Thermoforming ☐</td> <td>Finishing ☐</td> <td>Rec/Store/Packaging ☐</td> <td>Other ☐</td> </tr> <tr> <td>Large Fab ☐</td> <td>Composite ☐</td> <td>Supplier ☐</td> <td></td> </tr> </table>						Skid-tube ☐	Cross tube ☐	Water Jet ☐	Engineering ☐	Machining ☐	Small Fab ☐	Prod. Eng. Coord. ☐	Quality ☐	Thermoforming ☐	Finishing ☐	Rec/Store/Packaging ☐	Other ☐	Large Fab ☐	Composite ☐	Supplier ☐																																							
Skid-tube ☐	Cross tube ☐	Water Jet ☐	Engineering ☐																																																												
Machining ☐	Small Fab ☐	Prod. Eng. Coord. ☐	Quality ☐																																																												
Thermoforming ☐	Finishing ☐	Rec/Store/Packaging ☐	Other ☐																																																												
Large Fab ☐	Composite ☐	Supplier ☐																																																													
Date :		Step #:		QTY Effective :			MRB (QSI042) Approval																																																								
Description Work Order Deviation				Disposition				Completed By																																																							
								Lead hand / Supervisor Approval Verification																																																							
								QC / QA Coordinator Approval																																																							
Root Cause		FAULT CATEGORY																																																													
Environment ☐	Design ☐	Doc/Data ☐	Equip/Tooling ☐	Handling/Pre ☐	Material ☐	Internal Transport ☐	Tribal Knowledge ☐	LOA ☐	Substation ☐	Past Expiry Date ☐	Misidentified ☐	No Re-verification ☐	Operator ☐	Offset/Setup ☐	Supplier ☐	Training ☐	Use for Testing ☐	Poor Information ☐	Rushing ☐	Product Improvement ☐	Process Improvement ☐	Manufacturing Process ☐	Past Due ☐	Pressure/Forced ☐	Bending ☐	Centre Not Concentric ☐	Cracks ☐	Crimp/Kink/Ripple/Wave ☐	Cuffs ☐	Crushing ☐	Heat Treat ☐	Wave/Twist in Tube ☐	Marks/Chatter ☐	Temperature/Cure ☐	Set-up ☐	BOM/Route ☐	Broken/Damage/Defect ☐	Inspection Incomplete/Unqualified ☐	Contamination ☐	Countersink ☐	Cut Too Short ☐	Instructions Incomplete/Unclear ☐	Drill Holes ☐	Power Loss/Surge ☐	Folio/Program ☐	Grain ☐	Weld ☐	Wrong Stock Pulled ☐	Out of Sequence ☐	Off-set ☐	Mislabeled ☐	Fit/Function ☐	Misaligned/off center ☐	Positioned Wrong ☐	Outside Dimensions ☐	Over/Under tolerance ☐	Part Incorrect ☐	Part Lost/Missing ☐	Part Moved ☐	Drawing ☐	Finish ☐	Misread ☐	Turning Sequence ☐
OTHER :																																																															

Picklist Print

Monday, November 09, 2015 8:39:14 AM

Page 1

Work Order ID: 138686

138686

Parent Item: D3822-2KGY

D3822-2KGY

Parent Item Name: Vertical Tunnel, RH

Start Date: 11/9/2015

Required Date: 11/9/2015

Start Qty: 2.00

Required Qty: 2.00

Comments: IPP RevA: New issue DD verified by:EC v
Add Step 105 Dry Material 10/04/21 DL

IPP REv. B.

Component Item ID/ Item Name	Replacement Item ID	Mfg/ Purch	Bin Item	Primary Location	Last Location	Route Seq ID	Unit of Measure	Qty on Hand	Qty per Kit	Total Qty	Qty Issued	Date Issued	Status
MKYD6185S.080-P3-52068		Purchased		No		100	sf	2,718.120	7.8	15.60780			DAS 07 9-39

MKYD6185S 080-P3-52068

Kydex steel grey (52"x96"-.080)

Location	Loc Qty	Loc Code
SHED	1180	
m129546	347	
m129760	347	
m130383	486	
therm	1538.12	
121902	543.15	
122181	994.97	

15/11/09

15.6078 sq ft.

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____		DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐		AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐					
Date :		Step #:		QTY Effective :			MRB (QSI042) Approval 		
Description Work Order Deviation				Disposition					
				Completed By					
				Lead hand / Supervisor Approval Verification					
				QC / QA Coordinator Approval					

Root Cause				FAULT CATEGORY							
Environment	☐	No Re-verification	☐	Pressure/Forced	☐	Temperature/Cure	☐	Power Loss/Surge	☐	Positioned Wrong	☐
Design	☐	Operator	☐	Bending	☐	Set-up	☐	Folio/Program	☐	Outside Dimensions	☐
Doc/Data	☐	Offset/Setup	☐	Centre Not Concentric	☐	BOM/Route	☐	Grain	☐	Over/Under tolerance	☐
Equip/Tooling	☐	Supplier	☐	Cracks	☐	Broken/Damage/Defect	☐	Weld	☐	Part Incorrect	☐
Handling/Pre	☐	Training	☐	Crimp/Kink/Ripple/Wave	☐	Inspection Incomplete/Unqualified	☐	Wrong Stock Pulled	☐	Part Lost/Missing	☐
Material	☐	Use for Testing	☐	Cuffs	☐	Contamination	☐	Out of Sequence	☐	Part Moved	☐
Internal Transport	☐	Poor Information	☐	Crushing	☐	Countersink	☐	Off-set	☐	Drawing	☐
Tribal Knowledge	☐	Rushing	☐	Heat Treat	☐	Cut Too Short	☐	Mislabeled	☐	Finish	☐
LOA	☐	Product Improvement	☐	Wave/Twist in Tube	☐	Instructions Incomplete/Unclear	☐	Fit/Function	☐	Misread	☐
Substation	☐	Process Improvement	☐	Marks/Chatter	☐	Drill Holes	☐	Misaligned/off center	☐	Turning Sequence	☐
Past Expiry Date	☐	Manufacturing Process	☐	OTHER :							
Misidentified	☐	Past Due	☐								

DART AEROSPACE LTD		Work Order: 138686
Description: Vertical Tunnel, RH		Part Number: D3822-2KIV/KGY
Inspection Dwg: D3822	Rev: C	Page 1 of 1

FIRST ARTICLE INSPECTION CHECKLIST

☒ First Article ☐ Prototype

THERMOFORMING SECTION

Description	Accept	Reject	Method of Inspection	Comments
Inside Radii less than <u>N/A</u> "				
Shape Definition	✓			
Texture Retention	✓			
Material imperfections such as bumps, cracks, voids, scratching	✓			

Measured by: [Signature]

Date: 15/10/06

TRIMMING SECTION

Drawing Dimension	Tolerance	Actual Dimension	Accept	Reject	Method of Inspection	Comments
0.8	Min	0.85"	✓			
0.3	Min	0.34"	✓			
0.55	Min	0.60"	✓			
0.040	Min	0.047"	✓			
0.050	Min	0.062"	✓			

Measured by: DAS 07 [Signature]

Date: 15/11/09


Audited by: SB [Signature]


Date: NOV 09 2015

Prototype Approval: N/A

Date: N/A

Rev	Date	Change	Revised by	Approved
A	09.07.29	New Issue	KJ <u>[Signature]</u>	<u>[Signature]</u>

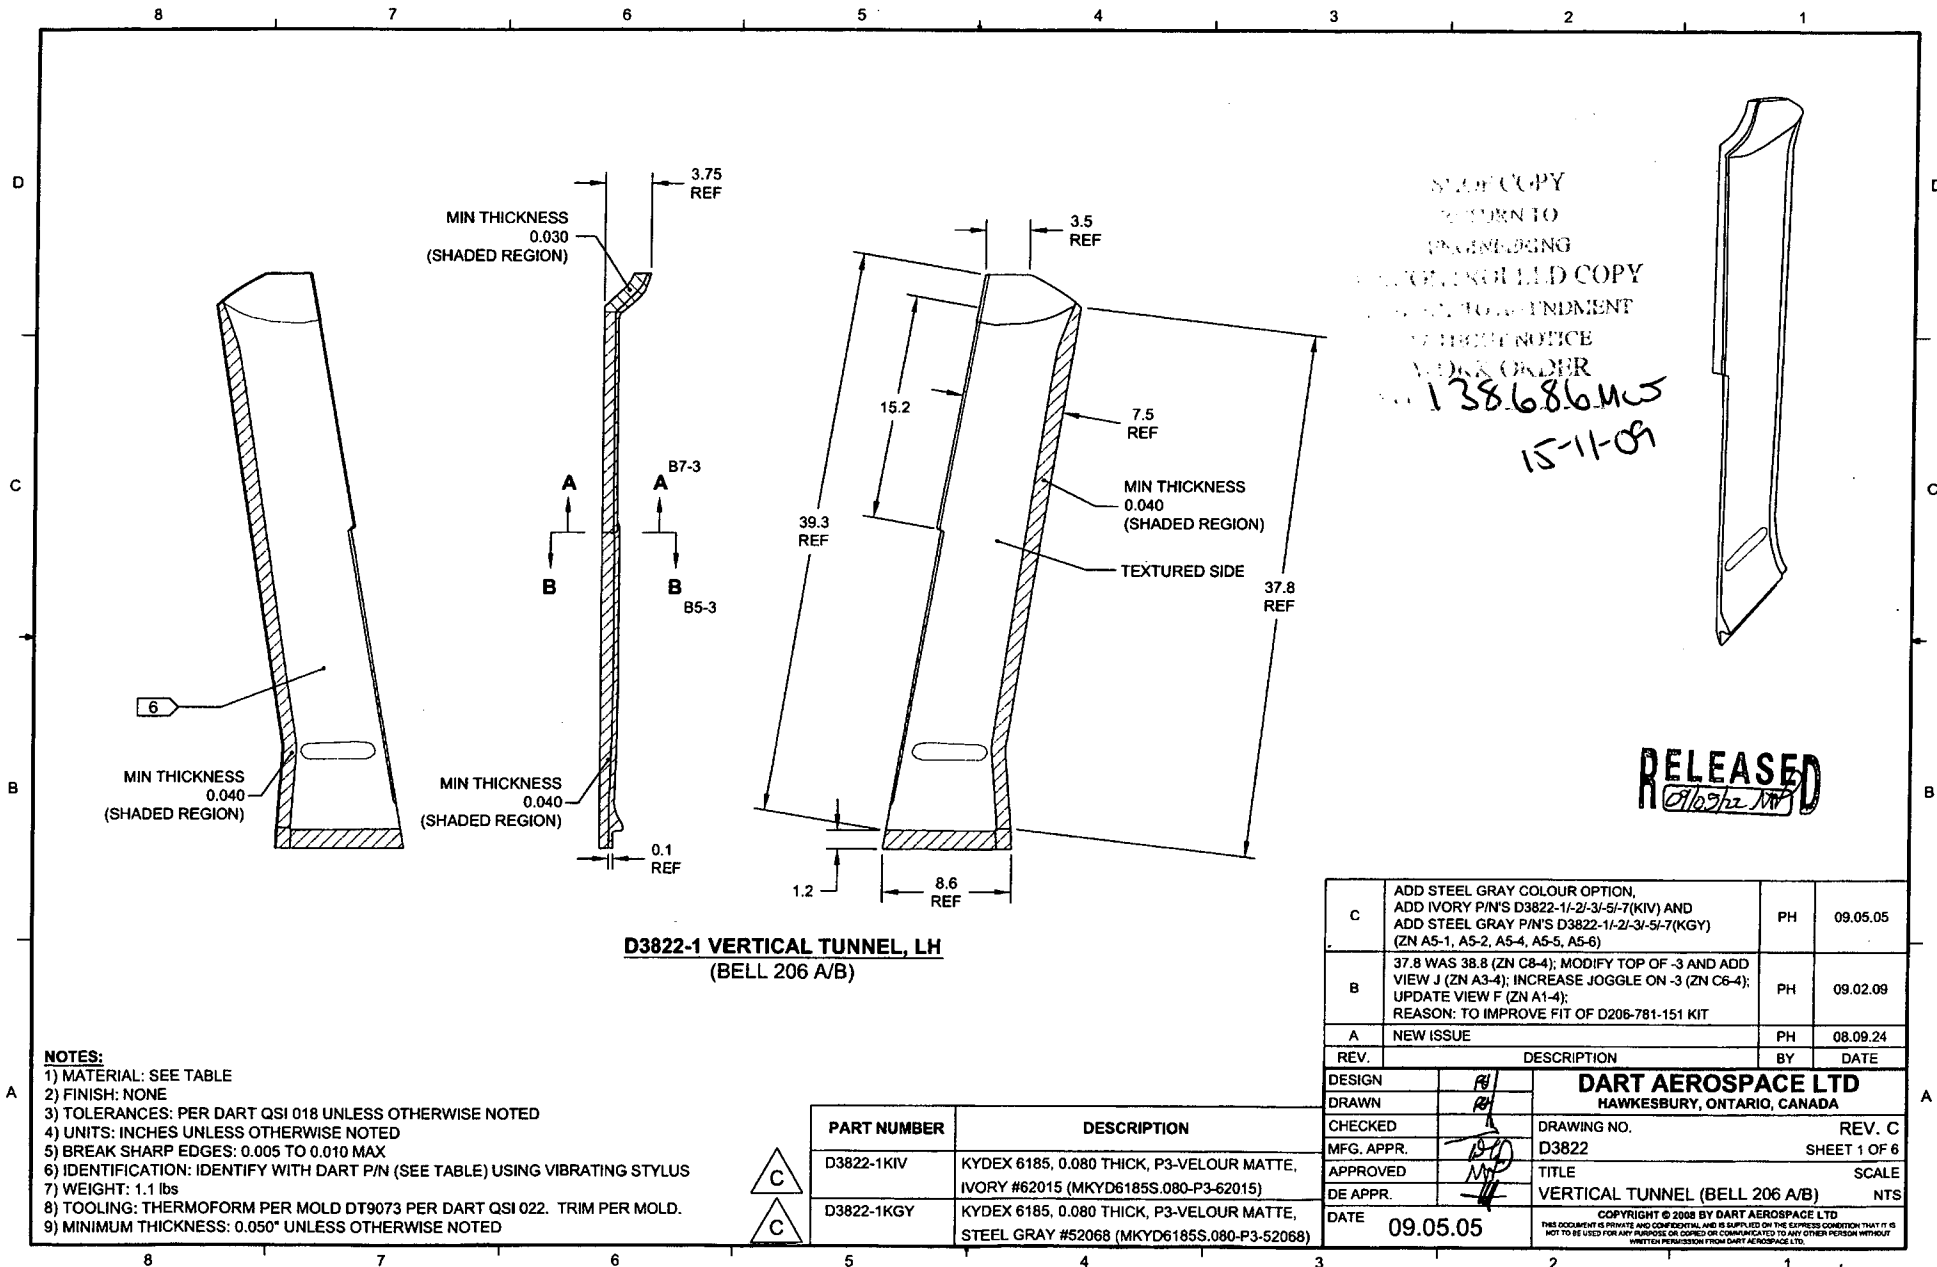

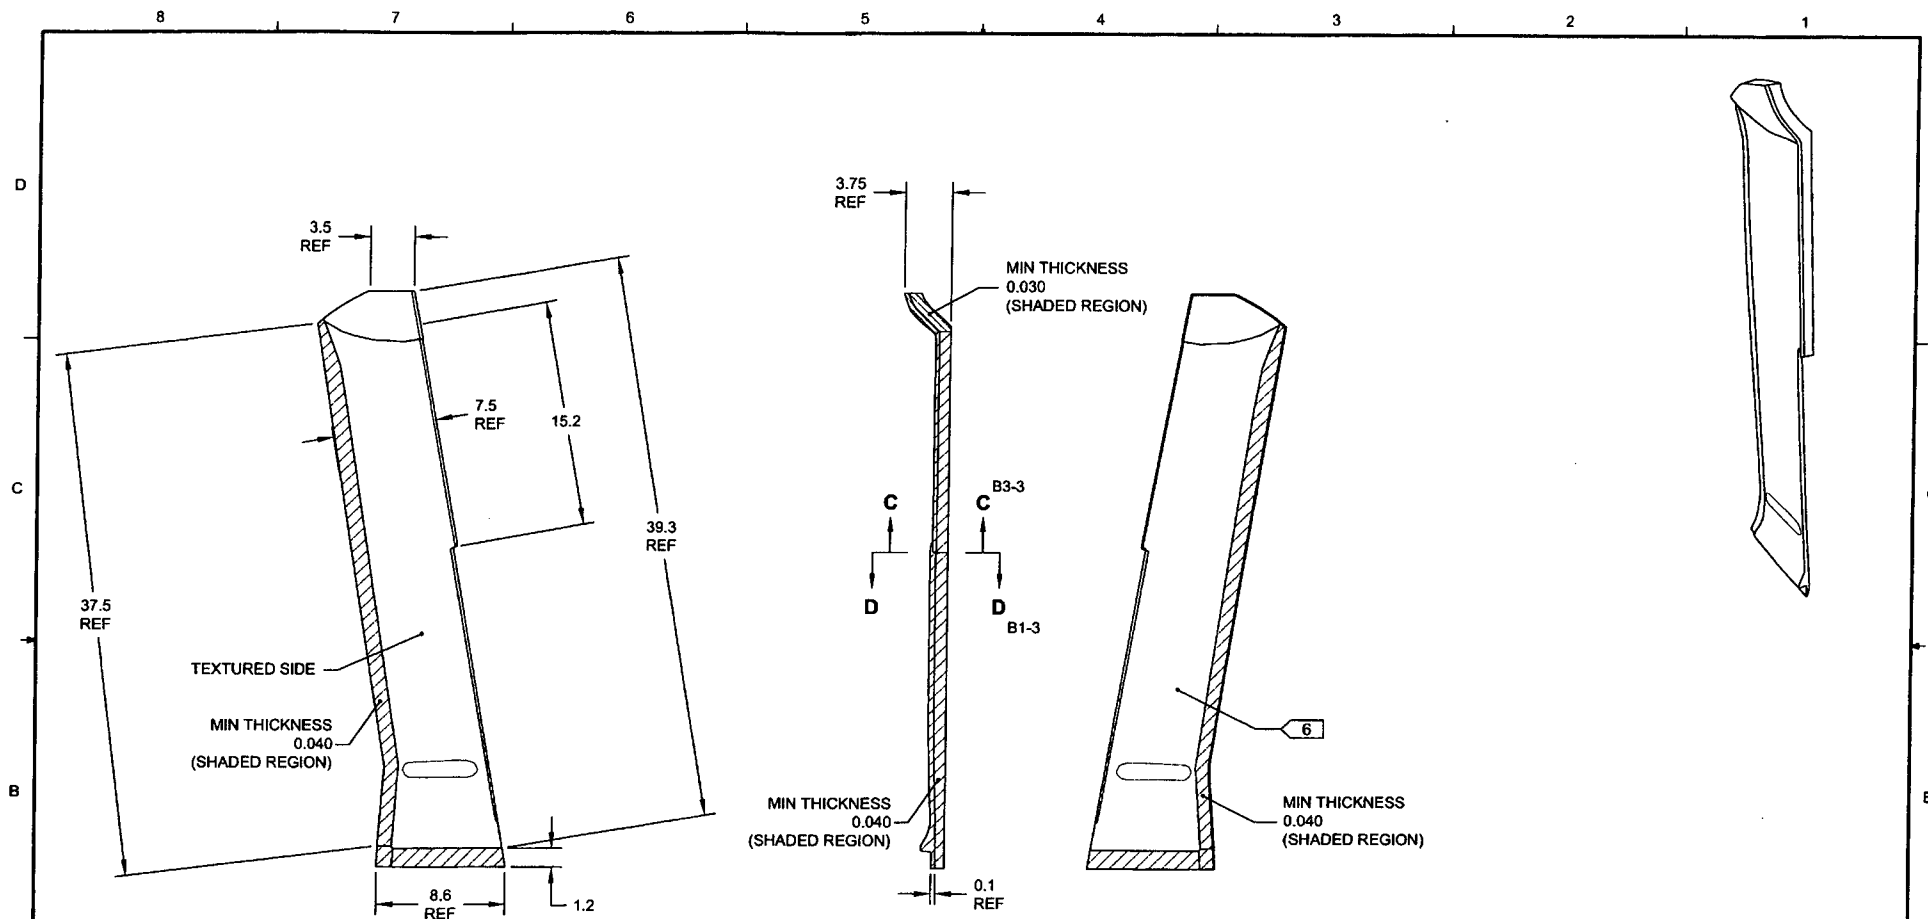

D3822-2 VERTICAL TUNNEL, RH
(BELL 206 A/B)

NOTES:


- 1) MATERIAL: SEE TABLE
- 2) FINISH: NONE
- 3) TOLERANCES: PER DART QSI 018 UNLESS OTHERWISE NOTED
- 4) UNITS: INCHES UNLESS OTHERWISE NOTED
- 5) BREAK SHARP EDGES: 0.005 TO 0.010 MAX
- 6) IDENTIFICATION: IDENTIFY WITH DART P/N (SEE TABLE) USING VIBRATING STYLUS
- 7) WEIGHT: 1.1 lbs
- 8) TOOLING: THERMOFORM PER MOLD DT9074 PER DART QSI 022. TRIM PER MOLD
- 9) MINIMUM THICKNESS: 0.050" UNLESS OTHERWISE NOTED




PART NUMBER	DESCRIPTION
D3822-2KIV	KYDEX 6185, 0.080 THICK, P3-VELOUR MATTE, IVORY #62015 (MKYD6185S.080-P3-62015)
D3822-2KGY	KYDEX 6185, 0.080 THICK, P3-VELOUR MATTE, STEEL GRAY #52068 (MKYD6185S.080-P3-52068)

DESIGN	PH	DART AEROSPACE LTD HAWKESBURY, ONTARIO, CANADA	
DRAWN	PH		
CHECKED	JA	DRAWING NO.	REV. C
MFG. APPR.	PH	D3822	SHEET 2 OF 6
APPROVED	PH	TITLE	SCALE
DE APPR.	PH	VERTICAL TUNNEL (BELL 206 A/B)	NTS
DATE	09.05.05	COPYRIGHT © 2005 BY DART AEROSPACE LTD THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS NOT TO BE USED FOR ANY PURPOSE OR COPIED OR COMMUNICATED TO ANY OTHER PERSON WITHOUT WRITTEN PERMISSION FROM DART AEROSPACE LTD.	


RELEASED
09/10/2022

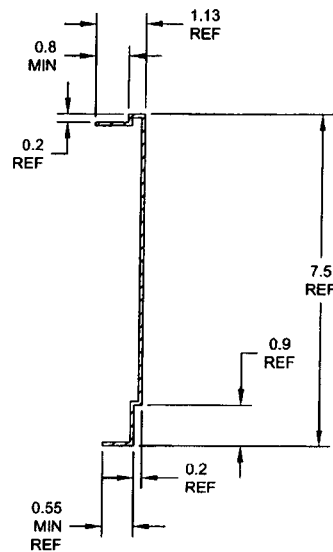


SECTION A-A C6-1

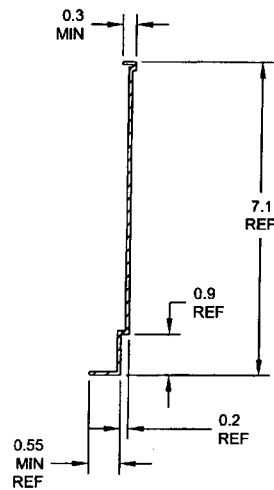

SECTION B-B C6-1

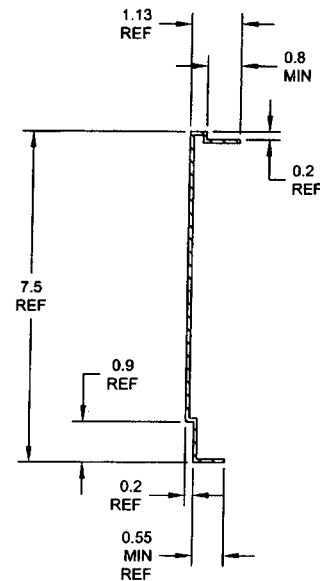

SECTION C-C C4-2

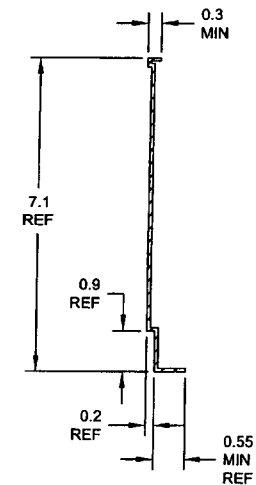


SECTION D-D C4-2

RELEASED
09/05/05

DESIGN	RA	DART AEROSPACE LTD	
DRAWN	RA	HAWKESBURY, ONTARIO, CANADA	
CHECKED	RA	DRAWING NO.	REV. C
MFG. APPR.	RA	D3822	SHEET 3 OF 6
APPROVED	RA	TITLE	SCALE
DE APPR.	RA	VERTICAL TUNNEL (BELL 206 A/B)	NTS
DATE	09.05.05	COPYRIGHT © 2005 BY DART AEROSPACE LTD THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS NOT TO BE USED FOR ANY PURPOSE OR COPIED OR COMMUNICATED TO ANY OTHER PERSON WITHOUT WRITTEN PERMISSION FROM DART AEROSPACE LTD.	

8 7 6 5 4 3 2 1

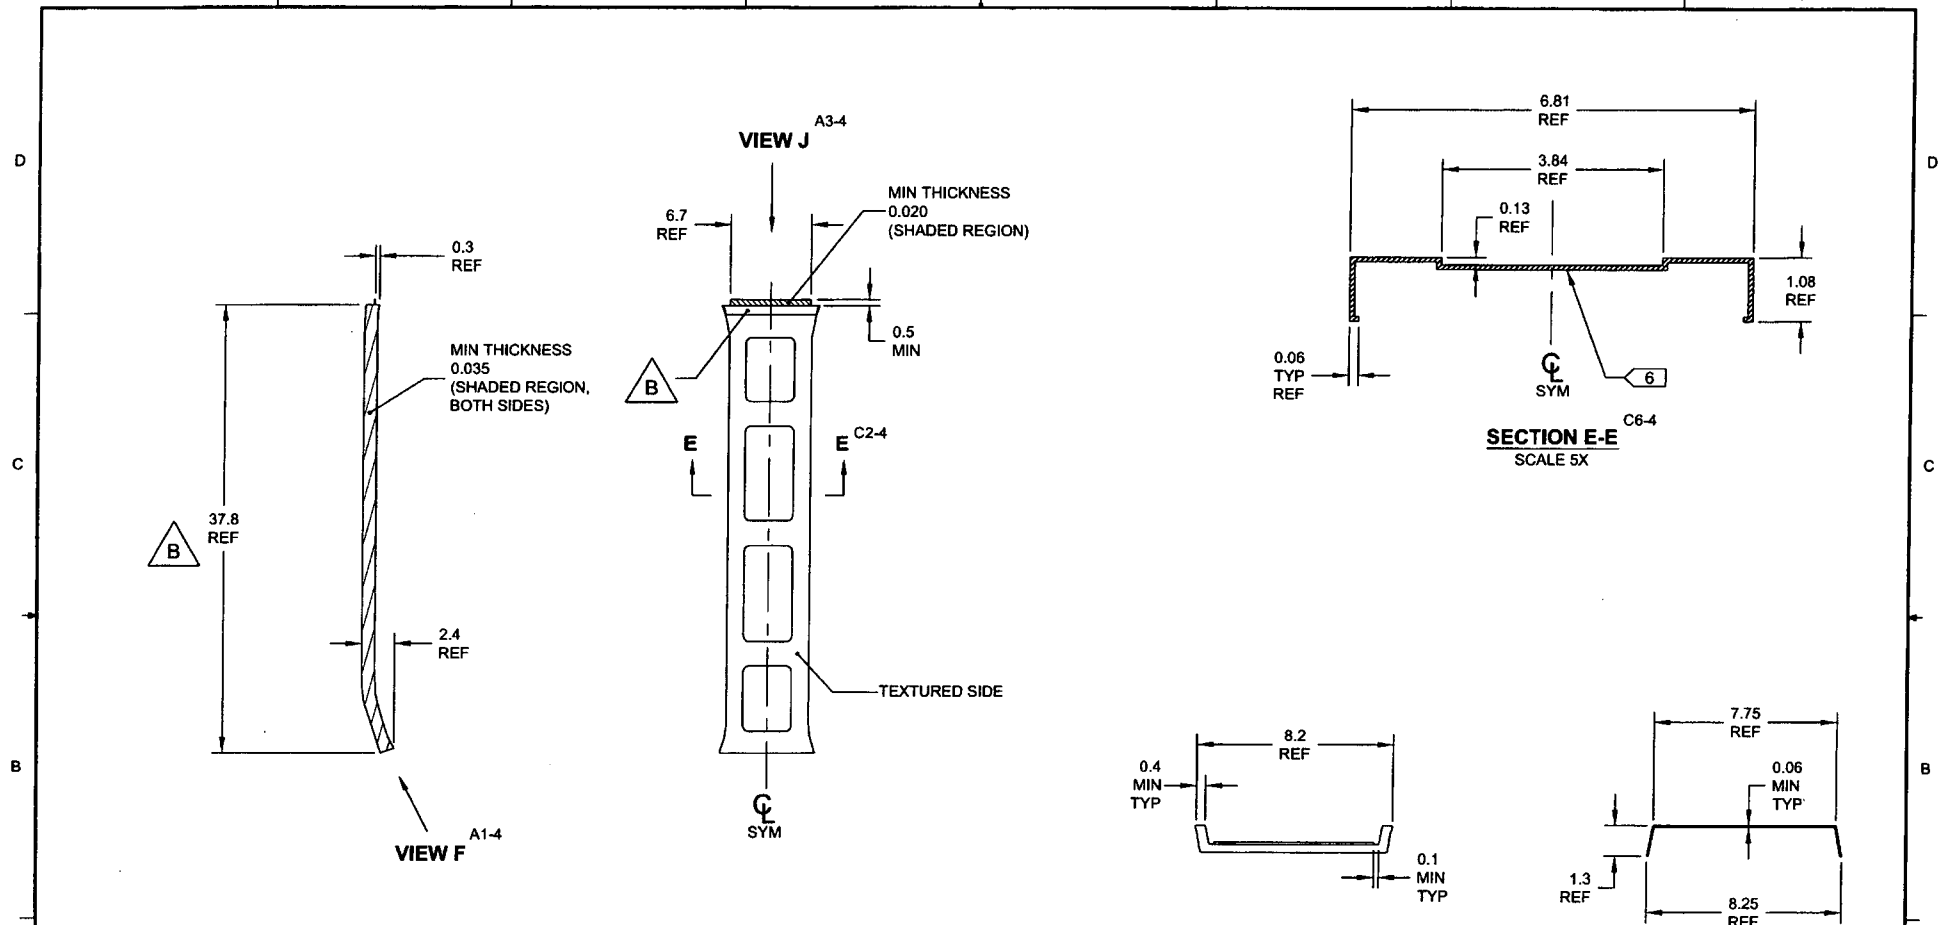

D3822-3 VERTICAL TUNNEL, AFT CENTER
(BELL 206 A/B)

VIEW J
SCALE 2X

RELEASED
09/05/22 MP

VIEW F
SCALE 2X
(ROTATED 90° CW)

NOTES:

- 1) MATERIAL: SEE TABLE
- 2) FINISH: NONE
- 3) TOLERANCES: PER DART QSI 018 UNLESS OTHERWISE NOTED
- 4) UNITS: INCHES UNLESS OTHERWISE NOTED
- 5) BREAK SHARP EDGES: 0.005 TO 0.010 MAX
- 6) IDENTIFICATION: IDENTIFY WITH DART P/N (SEE TABLE) USING VIBRATING STYLUS
- 7) WEIGHT: 1.1 lbs
- 8) TOOLING: THERMOFORM PER MOLD DT9072 PER DART QSI 022. TRIM PER MOLD
- 9) MINIMUM THICKNESS: 0.050" UNLESS OTHERWISE NOTED

C
C


PART NUMBER	DESCRIPTION
D3822-3KIV	KYDEX 6185, 0.080 THICK, P3-VELOUR MATTE, IVORY #62015 (MKYD6185S.080-P3-62015)
D3822-3KGY	KYDEX 6185, 0.080 THICK, P3-VELOUR MATTE, STEEL GRAY #52068 (MKYD6185S.080-P3-52068)

DESIGN	REV. C
DRAWN	D3822
CHECKED	REV. C
MFG. APPR.	SHEET 4 OF 6
APPROVED	TITLE
DE APPR.	VERTICAL TUNNEL (BELL 206 A/B)
DATE	09.05.05
	SCALE
	NTS

DART AEROSPACE LTD
HAWKESBURY, ONTARIO, CANADA

COPYRIGHT © 2008 BY DART AEROSPACE LTD
THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS NOT TO BE USED FOR ANY PURPOSE OR COPIED OR COMMUNICATED TO ANY OTHER PERSON WITHOUT WRITTEN PERMISSION FROM DART AEROSPACE LTD.

8 7 6 5 4 3 2 1

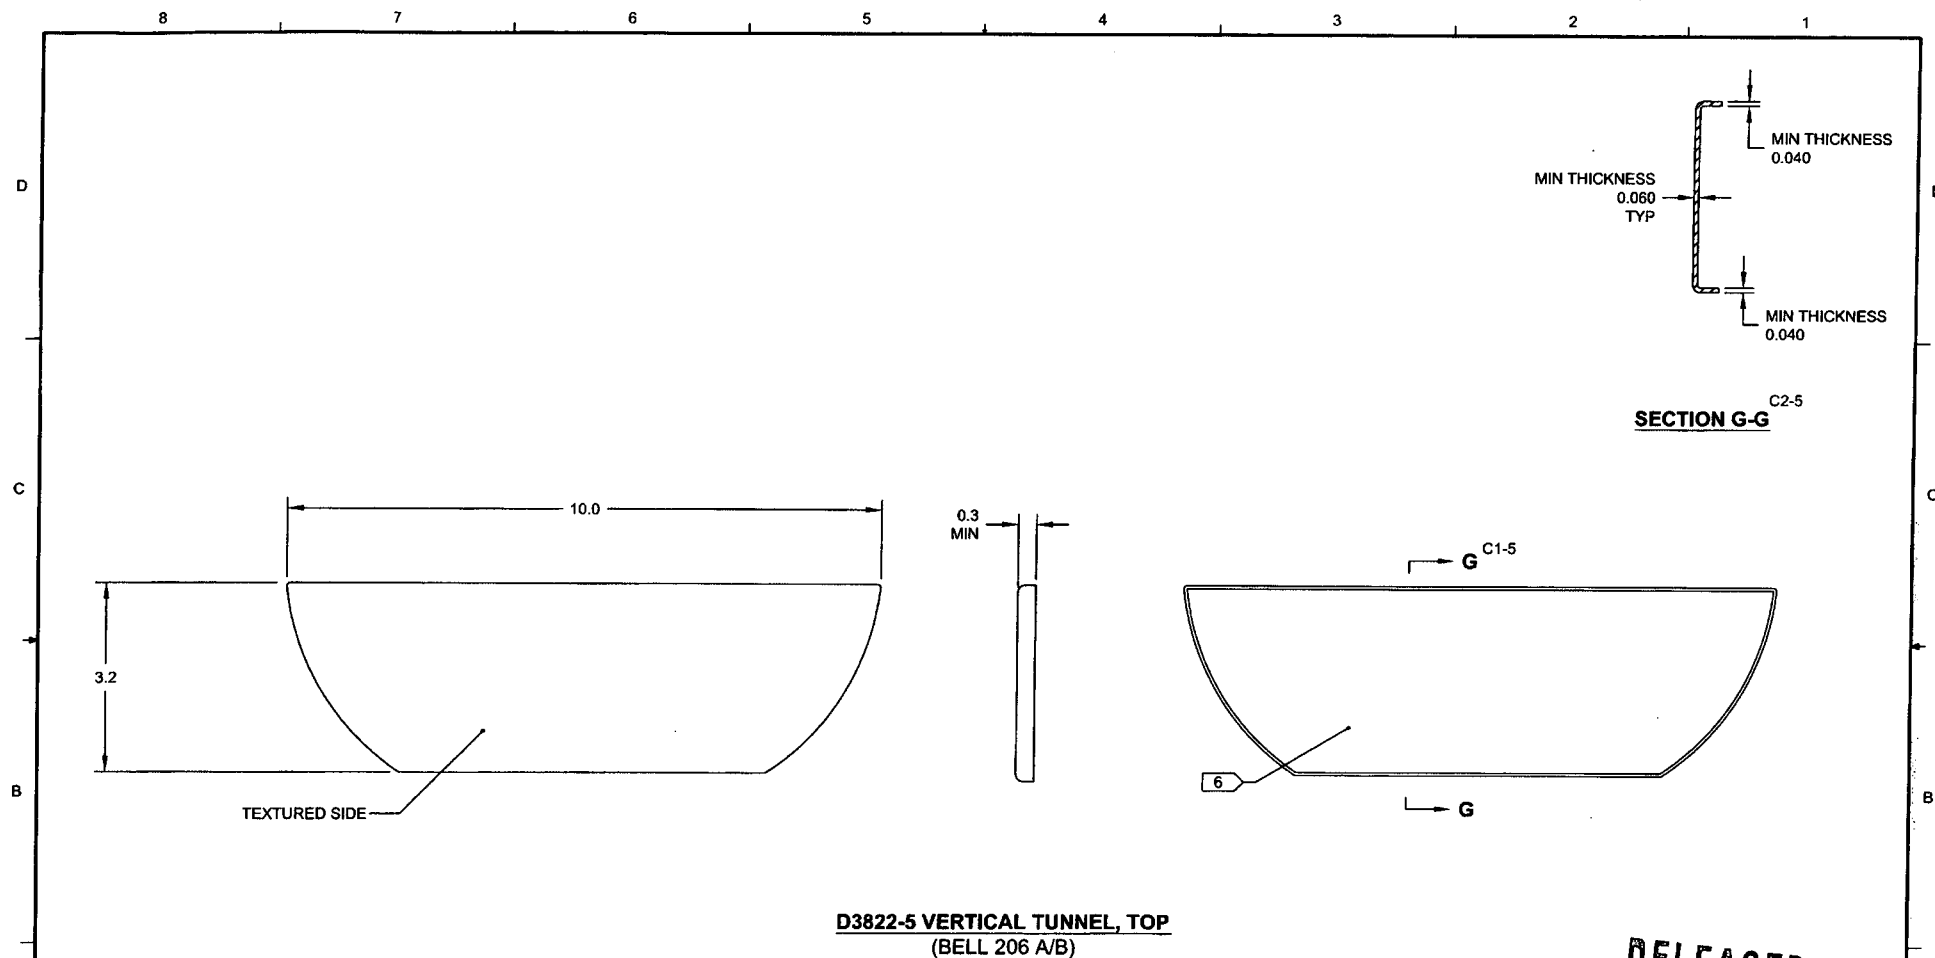

RELEASE
9/05/22 MP


NOTES:

- 1) MATERIAL: SEE TABLE
3) TOLERANCES: PER DART QSI 018 UNLESS OTHERWISE NOTED
4) UNITS: INCHES UNLESS OTHERWISE NOTED
5) BREAK SHARP EDGES: 0.005 TO 0.010 MAX
6) IDENTIFICATION: IDENTIFY WITH DART P/N (SEE TABLE) USING VIBRATING STYLUS
7) WEIGHT: 0.12 lbs
8) TOOLING: THERMOFORM PER MOLD DT9078 PER DART QSI 022

PART NUMBER	DESCRIPTION
D3822-5KIV	KYDEX 6185, 0.080 THICK, P3-VELOUR MATTE, IVORY #62015 (MKYD6185S.080-P3-62015)
D3822-5KGY	KYDEX 6185, 0.080 THICK, P3-VELOUR MATTE, STEEL GRAY #52068 (MKYD6185S.080-P3-52068)

DESIGN		DART AEROSPACE LTD	
DRAWN		HAWKESBURY, ONTARIO, CANADA	
CHECKED		DRAWING NO.	REV. C
MFG. APPR.		D3822	SHEET 5 OF 6
APPROVED		TITLE	SCALE
DE APPR.		VERTICAL TUNNEL (BELL 206 A/B)	NTS
DATE	09.05.05	COPYRIGHT © 2008 BY DART AEROSPACE LTD THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL AND IS SUPPLIED TO THE PURCHASER UNDER AGREEMENT THAT IT IS NOT TO BE USED FOR ANY PURPOSE OR COPIED OR REPRODUCED TO ANY OTHER PERSON WITHOUT THE WRITTEN PERMISSION FROM DART AEROSPACE LTD.	

COPYRIGHT © 2008 BY DART AEROSPACE LTD
THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS
NOT TO BE USED FOR ANY PURPOSE OR COPIED OR COMMUNICATED TO ANY OTHER PERSON WITHOUT
WRITTEN PERMISSION FROM DART AEROSPACE LTD

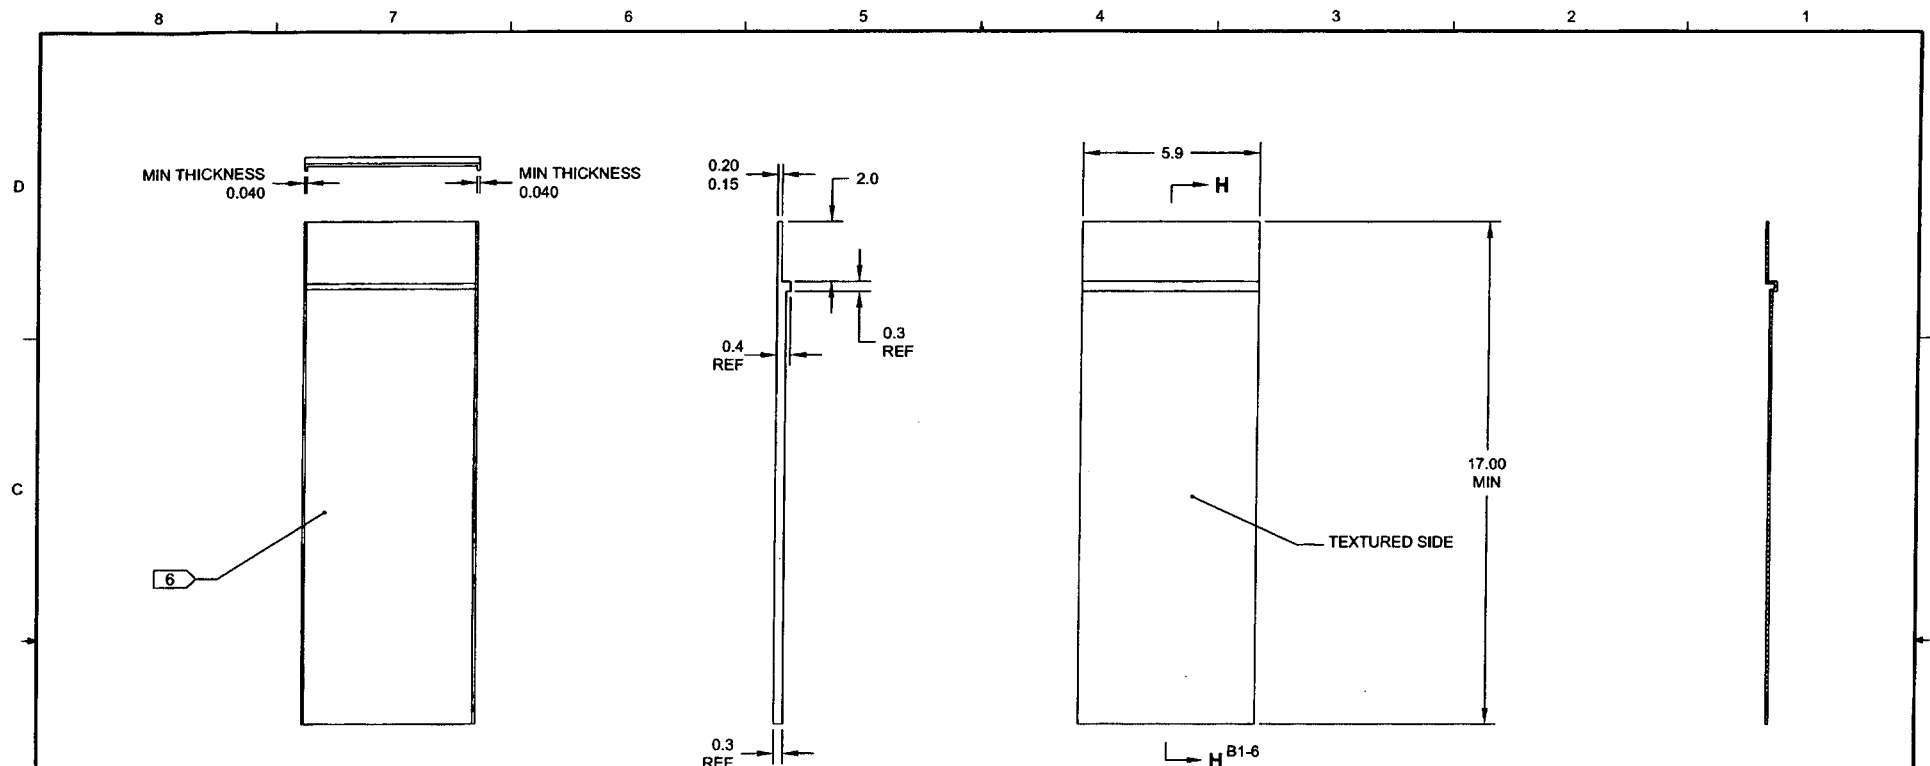

SECTION H-H B3-6

D3822-7 VERTICAL TUNNEL, LOWER
(BELL 206 A/B)

RELEASED
09/05/22

NOTES:

- 1) MATERIAL: SEE TABLE
- 2) FINISH: NONE
- 3) TOLERANCES: PER DART QSI 018 UNLESS OTHERWISE NOTED
- 4) UNITS: INCHES UNLESS OTHERWISE NOTED
- 5) BREAK SHARP EDGES: 0.005 TO 0.010 MAX
- 6) IDENTIFICATION: IDENTIFY WITH DART P/N (SEE TABLE) WITH VIBRATING STYLUS
- 7) WEIGHT: 0.36 lbs
- 8) TOOLING: THERMOFORM PER MOLD DT9396 PER DART QSI 022
- 9) MINIMUM THICKNESS: 0.060" UNLESS OTHERWISE NOTED



PART NUMBER	DESCRIPTION
D3822-7KIV	KYDEX 6185, 0.080 THICK, P3-VELOUR MATTE, IVORY #62015 (MKYD6185S.080-P3-62015)
D3822-7KGY	KYDEX 6185, 0.080 THICK, P3-VELOUR MATTE, STEEL GRAY #52068 (MKYD6185S.080-P3-52068)

DESIGN	PA	DART AEROSPACE LTD
DRAWN	BA	HAWKESBURY, ONTARIO, CANADA
CHECKED	PA	DRAWING NO. REV. C
MFG. APPR.	PA	D3822 SHEET 6 OF 6
APPROVED	PA	TITLE SCALE
DE APPR.	PA	VERTICAL TUNNEL (BELL 206 A/B) NTS
DATE	09.05.05	COPYRIGHT © 2006 BY DART AEROSPACE LTD
THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS NOT TO BE USED FOR ANY PURPOSE OR COPIED OR COMMUNICATED TO ANY OTHER PERSON WITHOUT WRITTEN PERMISSION FROM DART AEROSPACE LTD.		
